

Lab 2: Agile Backlog and Sprint Simulation

Second-Hand Escrow Marketplace

Samarth Mohan
PES1UG24CS703
Software Engineering Lab

September 6, 2026

Problem 39, Second-Hand Product Escrow Marketplace. Lab 1 input: FR-001..FR-005 with NFR-001 freeze.

1 Epics and User Stories

Company-managed Scrum project **SHEC** (board **SHEC board**). Three epics, seven stories, 42 story points on the Fibonacci scale.

Key	Summary	Epic	Priority	Pts
SHEC-5	Place order and pay to fund escrow	E1 Buyer Ordering	High	8
SHEC-6	Lock payment and set Under Inspection	E2 Escrow Trust	High	8
SHEC-9	Claim order and upload inspection report	E3 Inspection	Medium	5
SHEC-4	Browse and view verified product	E1 Buyer Ordering	High	3
SHEC-7	Freeze escrow on dispute	E2 Escrow Trust	High	5
SHEC-8	Release to seller or refund and Close	E2 Escrow Trust	High	5
SHEC-10	Review report and Approve or Dispute	E3 Inspection	Medium	8
			Total	42

Table 1: Backlog stories with epic rollups E1 = 11, E2 = 18, E3 = 13.




Figure 1: Backlog with Epics panel showing E1, E2, E3.

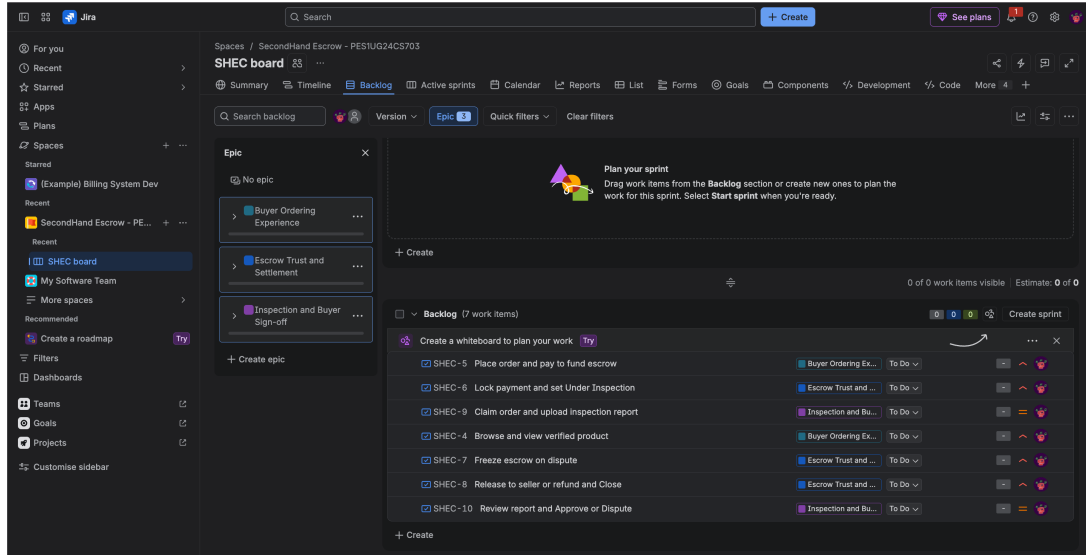


Figure 2: All 7 stories in rank order under their epics.

Story	Summary	Assignee	Status	Story Points
SHEC-5	Place order and pay to fund escrow	Buyer Ordering Ex...	To Do	8
SHEC-6	Lock payment and set Under Inspection	Escrow Trust and ...	To Do	8
SHEC-9	Claim order and upload inspection report	Inspection and Bu...	To Do	5
SHEC-4	Browse and view verified product	Buyer Ordering Ex...	To Do	3
SHEC-7	Freeze escrow on dispute	Escrow Trust and ...	To Do	5
SHEC-8	Release to seller or refund and Close	Escrow Trust and ...	To Do	5
SHEC-10	Review report and Approve or Dispute	Inspection and Bu...	To Do	8

Figure 3: Story Points column with epic rollups.

2 Sprint Plan

Sprint	Window	Goal	Scope (pts)
Sprint 1	Sep 1–Sep 6	Fund, lock, inspect	SHEC-5, 6, 9 (21/21)
Sprint 2	Aug 25–Sep 6	Approve/dispute, freeze, payout	SHEC-4, 7, 8, 10 (21/21)

Table 2: Sprint windows and delivered scope, as rendered in the burndown charts. Sprint 2 scope counted Sep 3; all 2026.

Disclosure: sprint windows were arranged to spread the simulation across the week (Sprint 1: Sep 1–Sep 6; Sprint 2 chart range: Aug 25–Sep 6); the burndown figures below are the authoritative record of scope and completion.

Simulated schedule, as read from the charts: Sprint 1, US-02 done Sep 2, US-03 Sep 3, US-06 Sep 4; Sprint 2, US-01 done Sep 4, US-04 Sep 5, US-05 Sep 5, US-07 Sep 6. Supporting worklogs mirror these days.

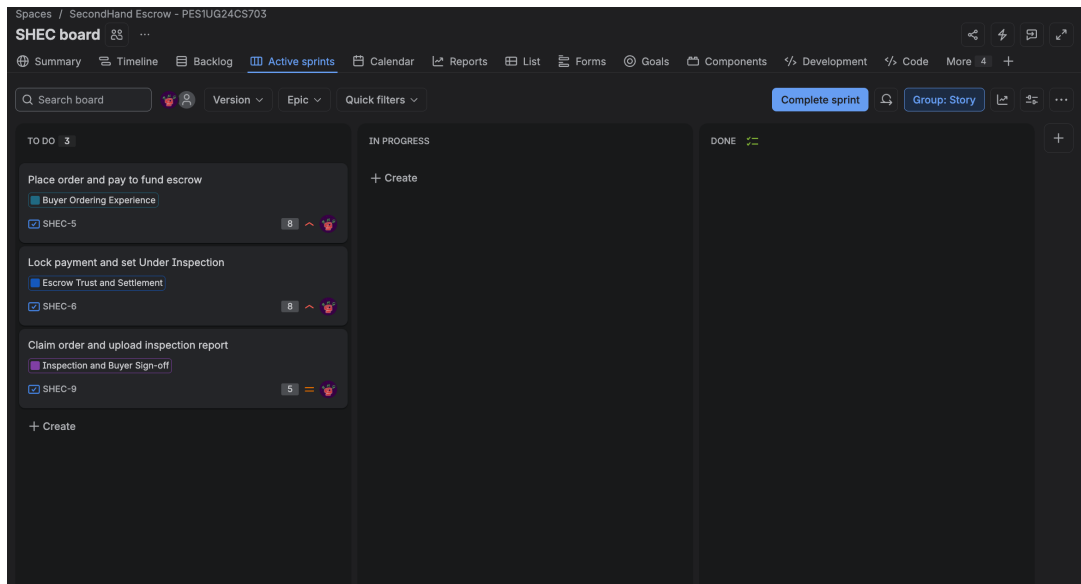


Figure 4: Sprint 1 Active Sprint view with scope in To Do.

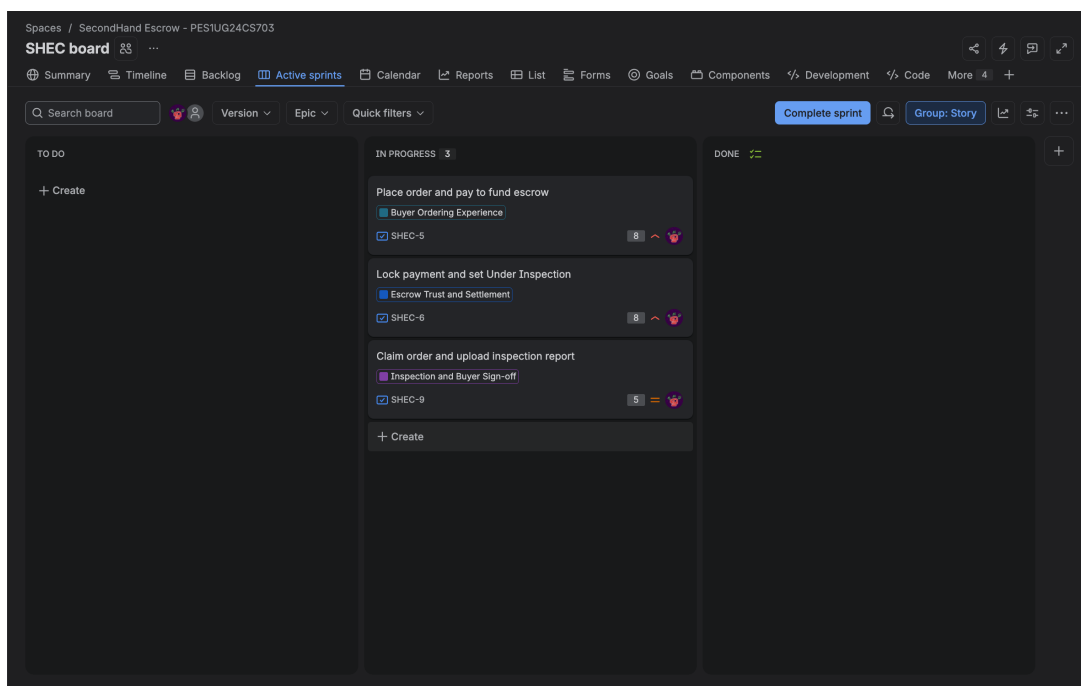


Figure 5: Sprint 1 Active Sprint view with scope In Progress.

Burndown Chart

Sprint 1 - Core Trust Flow Story Points ▾

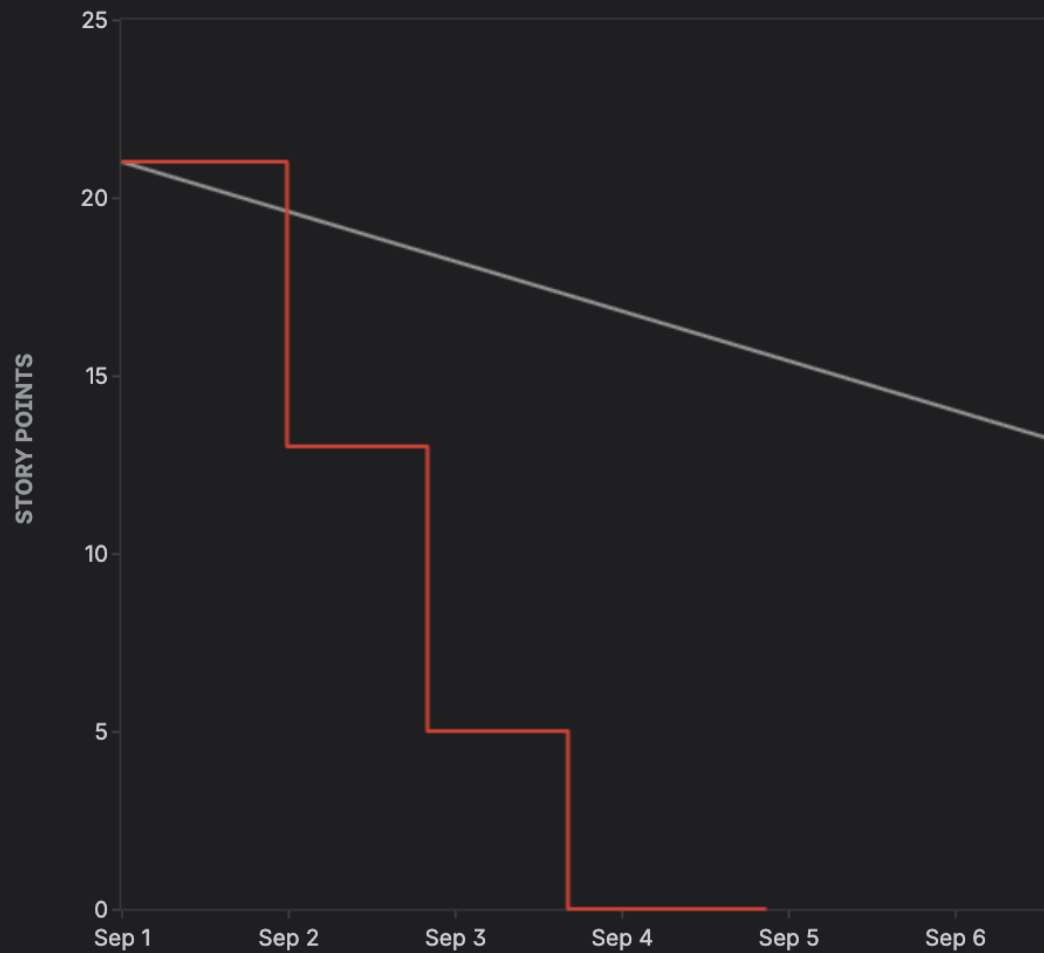


Figure 6: Sprint 1 burndown chart, Sep 1 to Sep 6, opening at 21 with drops on Sep 2, 3 and 4.

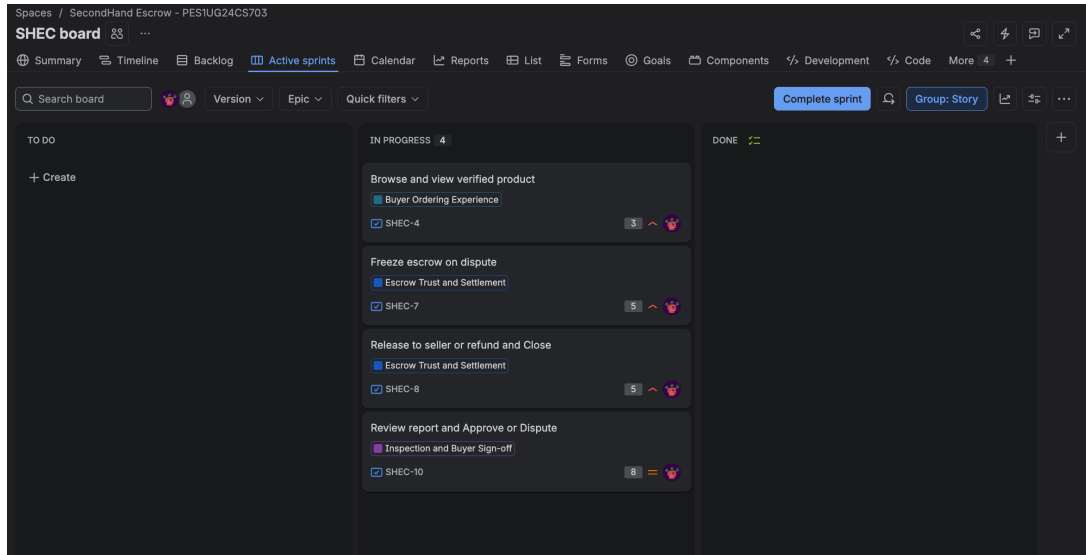


Figure 7: Sprint 2 Active Sprint view with scope In Progress.



Figure 8: Sprint 2 burndown chart, Aug 25 to Sep 6, scope 21 from Sep 3 with stepwise completion.

3 Burndown Observations

Sprint 1 opens at full scope (21) on Sep 1 with no mid-sprint scope change and burns down in three steps: 21 to 13 on Sep 2, 13 to 5 on Sep 3, 5 to 0 on Sep 4, holding at 0 through Sep 6. Sprint 2 ranges Aug 25 to Sep 6: remaining work reads 0 until Sep 3, when the sprint start counts the full scope of 21, then burns down in four steps: 21 to 18 late Sep 4, 18 to 13 and 13 to 8 across Sep 5, 8 to 0 on Sep 6. Neither sprint shows added scope after start, so scope creep is zero; both red lines finish at 0 inside their windows.

4 Reflection

1. Did your estimations reflect the actual effort? Relatively, yes: the 8-point gateway and dual-approval stories were the heaviest, the 3-point browse story the lightest, and nothing

spilled over. Absolutely, calibration is provisional, since one compressed session cannot validate durations; the 3-pointer may have been generous.

2. Was your backlog well-prioritized? Yes: Sprint 1 delivered the trust chain in dependency order (fund, then lock, then inspect), which unblocked Sprint 2 settlement (freeze, payout, approve). No story waited on a lower-ranked one.

3. How did your simulated sprint align with your plan? Scope aligned fully (21 of 21 in both sprints) and completion spread across the arranged windows exactly as planned (Sep 2/3/4 and Sep 4/5/6 respectively), as disclosed above.

4. What insights did the burndown chart give about your team's capacity? Demonstrated velocity is 21 points per 1-week sprint for this backlog mix, with steady multi-day burn (Sprint 1 done Sep 4, Sprint 2 Sep 6) rather than a last-day cliff, which suggests a sustainable pace for this team size and story mix.
